

(Bulletin for Statehouse, Capitol Mall Employees April 2, 2002)

Department of Administration  
Construction Update No. 33


## West Stairs Nearly Poured

**Ed Welsh, McAlvain Construction Superintendent**, reports that they have poured the west upper landing and five upper steps; Wednesday they will pour five more steps and by this Friday will pour the center landing and start on the lower steps. According to Ed, the concrete pouring is moving smoothly (*see photo at right*).

## Masonry Repair Work / Interior Investigations

**Project Manager Craig Vander Vorste, 3D/International**, says that the exterior masonry repair is on schedule (*see photos of south side scaffolding and east side scaffolding below.*) Also, the design group **CSHQA** is coordinating interior investigatory work which may include floor surfaces, ceiling surfaces, and some walls.

See *renewal news* online at: <http://www.idahocapitolcommission.org/whatsnew.html>

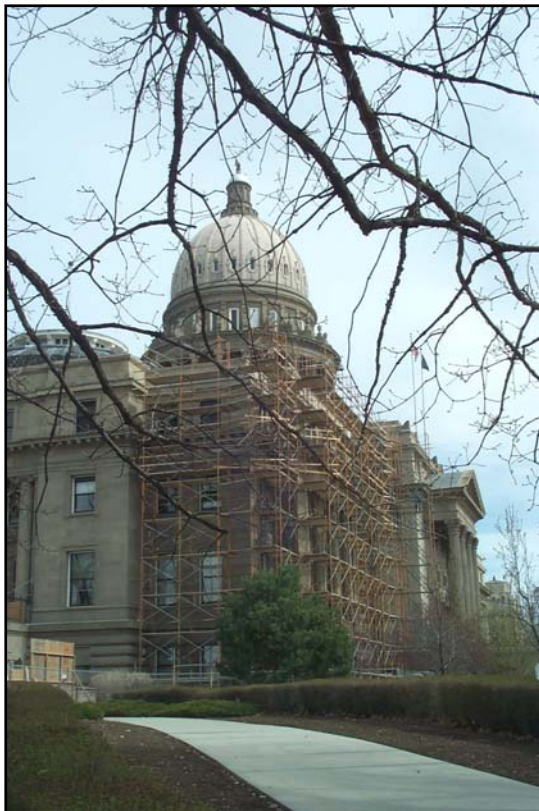

**Please note:** The intent of *renewal news* is to provide readers the most current and complete information as possible regarding construction activities during the Capitol Restoration project. **However, construction schedules are always subject to change, based upon weather conditions, transport and acquisition of support equipment and personnel, or other unforeseen circumstances.** Inquiries, comments on the Restoration effort can be sent to **Diane Blume** at [dblume@adm.state.id.us](mailto:dblume@adm.state.id.us). If you have questions about *renewal news* contact **Carole Schroeder** at 332-1802 or [cschroed@adm.state.id.us](mailto:cschroed@adm.state.id.us)

